



PUBLIC WORKS RIGHT-OF-WAY PERMIT

| | |
|----------------------------------|----------------------------|
| MAP & TAX LOT NUMBER: | PERMIT NUMBER: |
| PROPERTY ADDRESS: | FILE NUMBER: |
| PROPERTY OWNER: | APPLICATION DATE: |
| | EXPIRATION DATE: |
| OWNER ADDRESS: | CONTRACTOR: |
| OWNER PHONE: | CONTRACTOR ADDRESS: |
| | CONTRACTOR PHONE: |


WORK TO BE DONE: (applicant to check all that apply)

DRIVEWAY APPROACH
 CURB/ GUTTER
 UTILITY INSTALLATION
 ROAD REPAIR
 EROSION CONTROL
 DITCH/ CULVERT
 SIDEWALK
 OTHER: _____

APPLICANT IS REQUIRED TO PROVIDE:
 (To be completed by City Staff)

TRAFFIC CONTROL
 EROSION CONTROL
 PROVIDE 24 HR PUBLIC NOTICE
 BOND
 OTHER: _____

- STREET REPAIR REQUIREMENTS:**
- 1) All construction shall meet or exceed Lincoln City standards and specifications.
 - 2) Property owner shall be responsible for condition of street repair for one (1) year after certificate of occupancy issued.
 - 3) Crushed rock in pipe zone will be compacted by vibratory plate or jumping jack per current APWA specifications.
 - 4) Contractor is responsible for plating trench while CLSM backfill material cures.
 - 5) Tee cut for asphalt patching will be made after trench excavation And backfill. Edges of cut shall be free of any spalling, Broken edges, cracks, uplift and undermined subgrade.
 - 6) If hot mix is unavailable, the contractor shall use cold mix as a temporary patch until hot mix is available for permanent repair.
 - 7) All edges of permanent patching shall be tack and sand sealed.
 - 8) Patching of trench shall be completed no later than two (2) days after installation inspection. The City reserves the right to make repairs and bill the contractor accordingly if patching has not been completed as required per the above notes.
 - 9) Asphalt patch shall be compacted to 92% density, minimum with a maximum surface smoothness deviation of 1/8 inch per APWA specification 00756.55(a).
 - 10) In the event of street closures due to construction, the contractor must notify emergency services and Public Works a minimum of 48-hours in advance. The contractor is also responsible for erecting proper signage, arranging detour routes, and traffic control devices per the Manual of Uniform Traffic Control Devices and Oregon standards.
 - 11) The contractor shall schedule inspections a minimum of 48-hours in advance with Public Works.

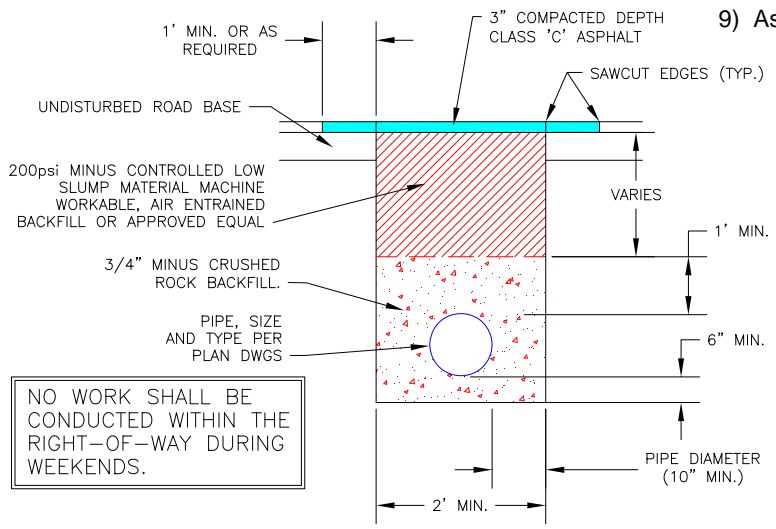

| | |
|--------------------------------------------------|---------------------------|
| Applicant has read the Above requirements | _____ (Initials and Date) |
| PERMIT FEE | = \$ _____ |
| DIRECTOR OF PUBLIC WORKS; or | DATE |
| CITY ENGINEER | DATE |
